



Phase name	Qty
Phase 1	30

General Notes: All steelwork to comply with SANS 2001:CS1 & SANS 1921-3
All profile notches to have 11mm radius unless noted otherwise

HARD STAMP	QUALITY CONTROL	
YS	NAME:	
	DATE COMPLETE:	
	CHECKED BY:	
	RELEASE DATE	

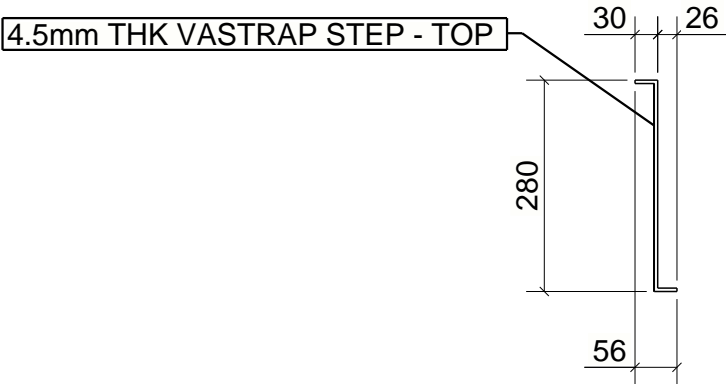

Top View



Back View

Material list for 30 parts named 'Vastrap Step'					
Mark	Profile	Grade	Length	Paint Area	Mass
M11	VT4.5*330.5	S355JR	1090	0.7	12.7
Total for 30 parts			32700	22.0	381.8

The part shown is required for the following assemblies:-		
1	required for 'Vastrap Step' assemblies marked A1	
29	required for 'Vastrap Step' assemblies marked A2	

Rev	Mark	Revision Description	Date
1	1	FOR CONSTRUCTION	08.10.2025



OGILVIE ENGINEERING
COTSWOLD CHECKERS
YARD STEEL STAIR
Cotswold Estate, Hillcrest, Durban KZN

Detailed by
Precise Structural Modelling
Office +27 31 2056906
Cell +27 83 779 1091
rowan@psmod.co.za



Drawn	J.P.R
Scale	1:10
Issued	08.10.2025
Revised	08.10.2025
Project Number	PSM 25179

Workshop Drawing

W	[M.11]	Rev	1
---	--------	-----	---
