
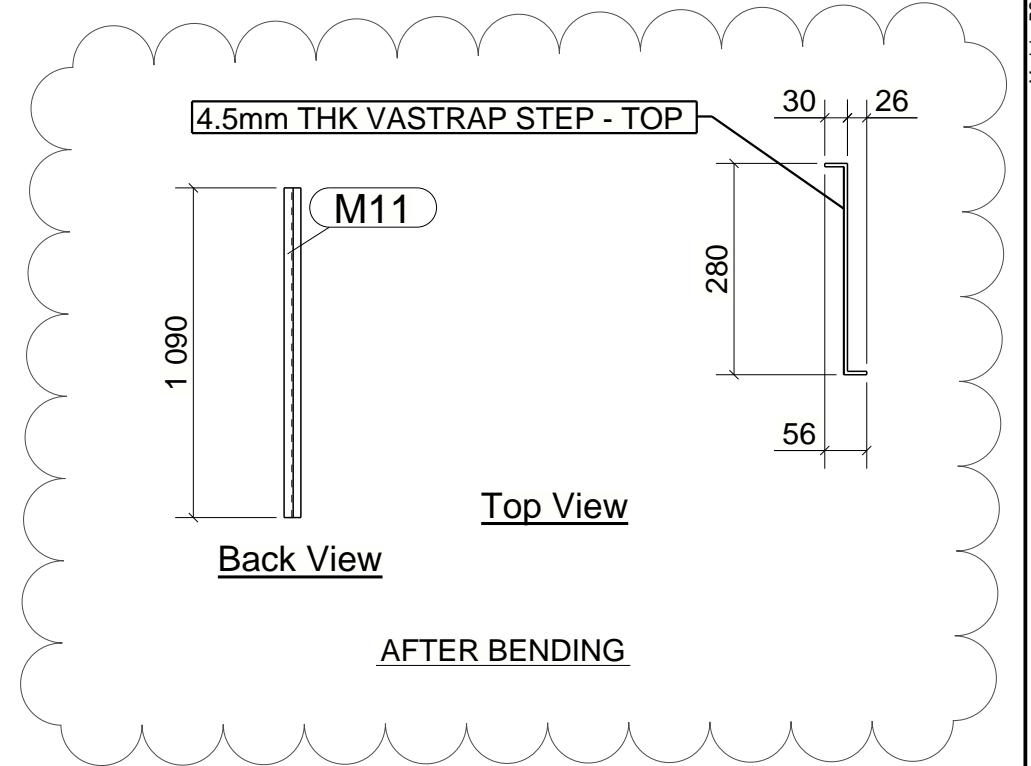


Phase name	Qty
Phase 1	30

General Notes: All steelwork to comply with SANS 2001:CS1 & SANS 1921-3
All profile notches to have 11mm radius unless noted otherwise

HARD STAMP	QUALITY CONTROL	
YS	NAME:	
	DATE COMPLETE:	
	CHECKED BY:	
	RELEASE DATE	

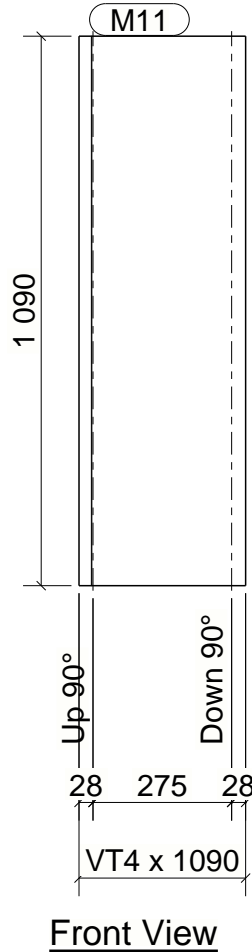

Material list for 30 parts named 'Vastrap Step'				
Mark	Profile	Grade	Length	Paint Area
M11	VT4.5*330.5	S355JR	1090	0.7
Total for 30 parts			32700	22.0
The part shown is required for the following assemblies:-				
1	required for 'Vastrap Step' assemblies marked A1			
29	required for 'Vastrap Step' assemblies marked A2			



OGILVIE ENGINEERING

COTSWOLD CHECKERS

YARD STEEL STAIR

Cotswold Estate, Hillcrest, Durban KZN

Detailed by

Precise Structural Modelling

Office +27 31 2056906
Cell +27 83 779 1091
rowan@psmod.co.za

Tekla Structures

Drawn	J.P.R
Scale	1:10 1:15
Issued	
Revised	
Project Number	PSM 25179

Workshop Drawing

W [M.11 - 1]

Rev
